ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1			**ENTERPRISE ICT SYSTEM ROLLOUT**	**79 days**	**Thu 2/1/25**	**Tue 22/4/25**	
2			**PHASE 1**	**10 days**	**Thu 2/1/25**	**Wed 15/1/25**	
3			**PROJECT INITIATION**	**10 days**	**Thu 2/1/25**	**Wed 15/1/25**	
4			Project Kick-Off Meeting	1 day	Thu 2/1/25	Thu 2/1/25	
5			Letter of Award (LOA) Received	1 day	Fri 3/1/25	Fri 3/1/25	4
6			Project Charter drafted	3 days	Mon 6/1/25	Wed 8/1/25	5
7			Project Charter approve - MILESTON	0 days	Wed 8/1/25	Wed 8/1/25	6
8			Stakeholder register created	2 days	Thu 9/1/25	Fri 10/1/25	7
9			Communication plan established	2 days	Mon 13/1/25	Tue 14/1/25	8
10			Weekly status report #1 distribute to stakeholders	1 day	Wed 15/1/25	Wed 15/1/25	9
11			**PHASE 2**	**14 days**	**Thu 16/1/25**	**Tue 4/2/25**	
12			**Requirements and Planning**	**14 days**	**Thu 16/1/25**	**Tue 4/2/25**	
13			BRS sessions conducted with client stakeholders	2 days	Thu 16/1/25	Fri 17/1/25	10
14			BRS document drafted	3 days	Mon 20/1/25	Wed 22/1/25	13
15			BRS reviewed and signed off by client - MILESTONE	0 days	Wed 22/1/25	Wed 22/1/25	14
16			SRS drafted	4 days	Thu 23/1/25	Tue 28/1/25	15
17			SRS reviewed and approved	2 days	Wed 29/1/25	Thu 30/1/25	16
18			Master project schedule developed and baseline - MILESTONE	0 days	Thu 30/1/25	Thu 30/1/25	17
19			Risk Register established	2 days	Fri 31/1/25	Mon 3/2/25	18
20			Weekly status report #2 distributed to stakeholders	1 day	Tue 4/2/25	Tue 4/2/25	19
21			**PHASE 3**	**22 days**	**Wed 5/2/25**	**Thu 6/3/25**	
22			**System Development and Intergration**	**22 days**	**Wed 5/2/25**	**Thu 6/3/25**	
23			**Workstream A - Portal and User Management**	**21 days**	**Wed 5/2/25**	**Wed 5/3/25**	
24			Portal architecture design	5 days	Wed 5/2/25	Tue 11/2/25	20
25			User Management module develo	10 days	Wed 12/2/25	Tue 25/2/25	24
26			Portal module development	10 days	Wed 5/2/25	Tue 18/2/25	24SS
27			Internal system testing	5 days	Wed 26/2/25	Tue 4/3/25	25,26
28			Weekly status report #3 distributed to stakeholders	1 day	Wed 5/3/25	Wed 5/3/25	27
29			**Workstream B - Data Migration**	**13 days**	**Wed 5/2/25**	**Fri 21/2/25**	
30			Data extraction from legacy systen	5 days	Wed 5/2/25	Tue 11/2/25	20
31			Data cleansing and validation scrip	5 days	Wed 12/2/25	Tue 18/2/25	30
32			Data migration dry run	3 days	Wed 19/2/25	Fri 21/2/25	31
33			Data migration sign-off - MILESTOI	0 days	Fri 21/2/25	Fri 21/2/25	32
34			**Workstream C - System Intergratior**	**19 days**	**Wed 5/2/25**	**Mon 3/3/25**	
35			Intergration test enviroment setup	3 days	Wed 5/2/25	Fri 7/2/25	20
36			Intergration testing Phase 1	7 days	Mon 10/2/25	Tue 18/2/25	35
37			Intergration testing Phase 2	7 days	Wed 19/2/25	Thu 27/2/25	36
38			Intergration sign-off	2 days	Fri 28/2/25	Mon 3/3/25	37
39			**Workstream D - Infrastructure and Deployment Planning**	**15 days**	**Wed 5/2/25**	**Tue 25/2/25**	
40			Server provisioning	5 days	Wed 5/2/25	Tue 11/2/25	20
41			Enviroment configuration	5 days	Wed 12/2/25	Tue 18/2/25	40
42			Deployment checklist prepared	3 days	Wed 19/2/25	Fri 21/2/25	41
43			Deployment readiness confirm	2 days	Mon 24/2/25	Tue 25/2/25	42
44			Weekly status report #4 distribute to stakeholders	1 day	Thu 6/3/25	Thu 6/3/25	28,33,38,43
45			**PHASE 4**	**25 days**	**Fri 7/3/25**	**Thu 10/4/25**	
46			**Testing and Acceptance**	**25 days**	**Fri 7/3/25**	**Thu 10/4/25**	
47			UAT plan prepare and distributed to (	2 days	Fri 7/3/25	Mon 10/3/25	44
48			UAT conducted with client stakehold	7 days	Tue 11/3/25	Wed 19/3/25	47
49			UAT defects logged and resolved	5 days	Thu 20/3/25	Wed 26/3/25	48
50			UAT sign-off by client -MILESTONE	0 days	Wed 26/3/25	Wed 26/3/25	49
51			FAT conducted with client stakehold	5 days	Thu 27/3/25	Wed 2/4/25	50
52			FAT defects logged and resolved	3 days	Thu 3/4/25	Mon 7/4/25	51
53			FAT sign-off by client - MILESTONE	0 days	Mon 7/4/25	Mon 7/4/25	52
54			Go-Live readiness checklist complete	2 days	Tue 8/4/25	Wed 9/4/25	53
55			weekly status report #5 distributed to stakeholders	1 day	Thu 10/4/25	Thu 10/4/25	54
56			**PHASE 5**	**8 days**	**Thu 10/4/25**	**Tue 22/4/25**	
57			**Deployment and Close-out**	**8 days**	**Thu 10/4/25**	**Tue 22/4/25**	
58			Go-Live deployment executed - MILESTONE	0 days	Thu 10/4/25	Thu 10/4/25	55
59			Post-deployment monitoring	5 days	Fri 11/4/25	Thu 17/4/25	58
60			Handover documentation prepared	3 days	Fri 11/4/25	Tue 15/4/25	58
61			Client training conducted	2 days	Wed 16/4/25	Thu 17/4/25	60
62			Project close-out report submitted	2 days	Fri 18/4/25	Mon 21/4/25	61
63			Weekly status report #6 distributed to stakeholders	1 day	Tue 22/4/25	Tue 22/4/25	62
64			Project formally close -MILESTONE	0 days	Tue 22/4/25	Tue 22/4/25	63

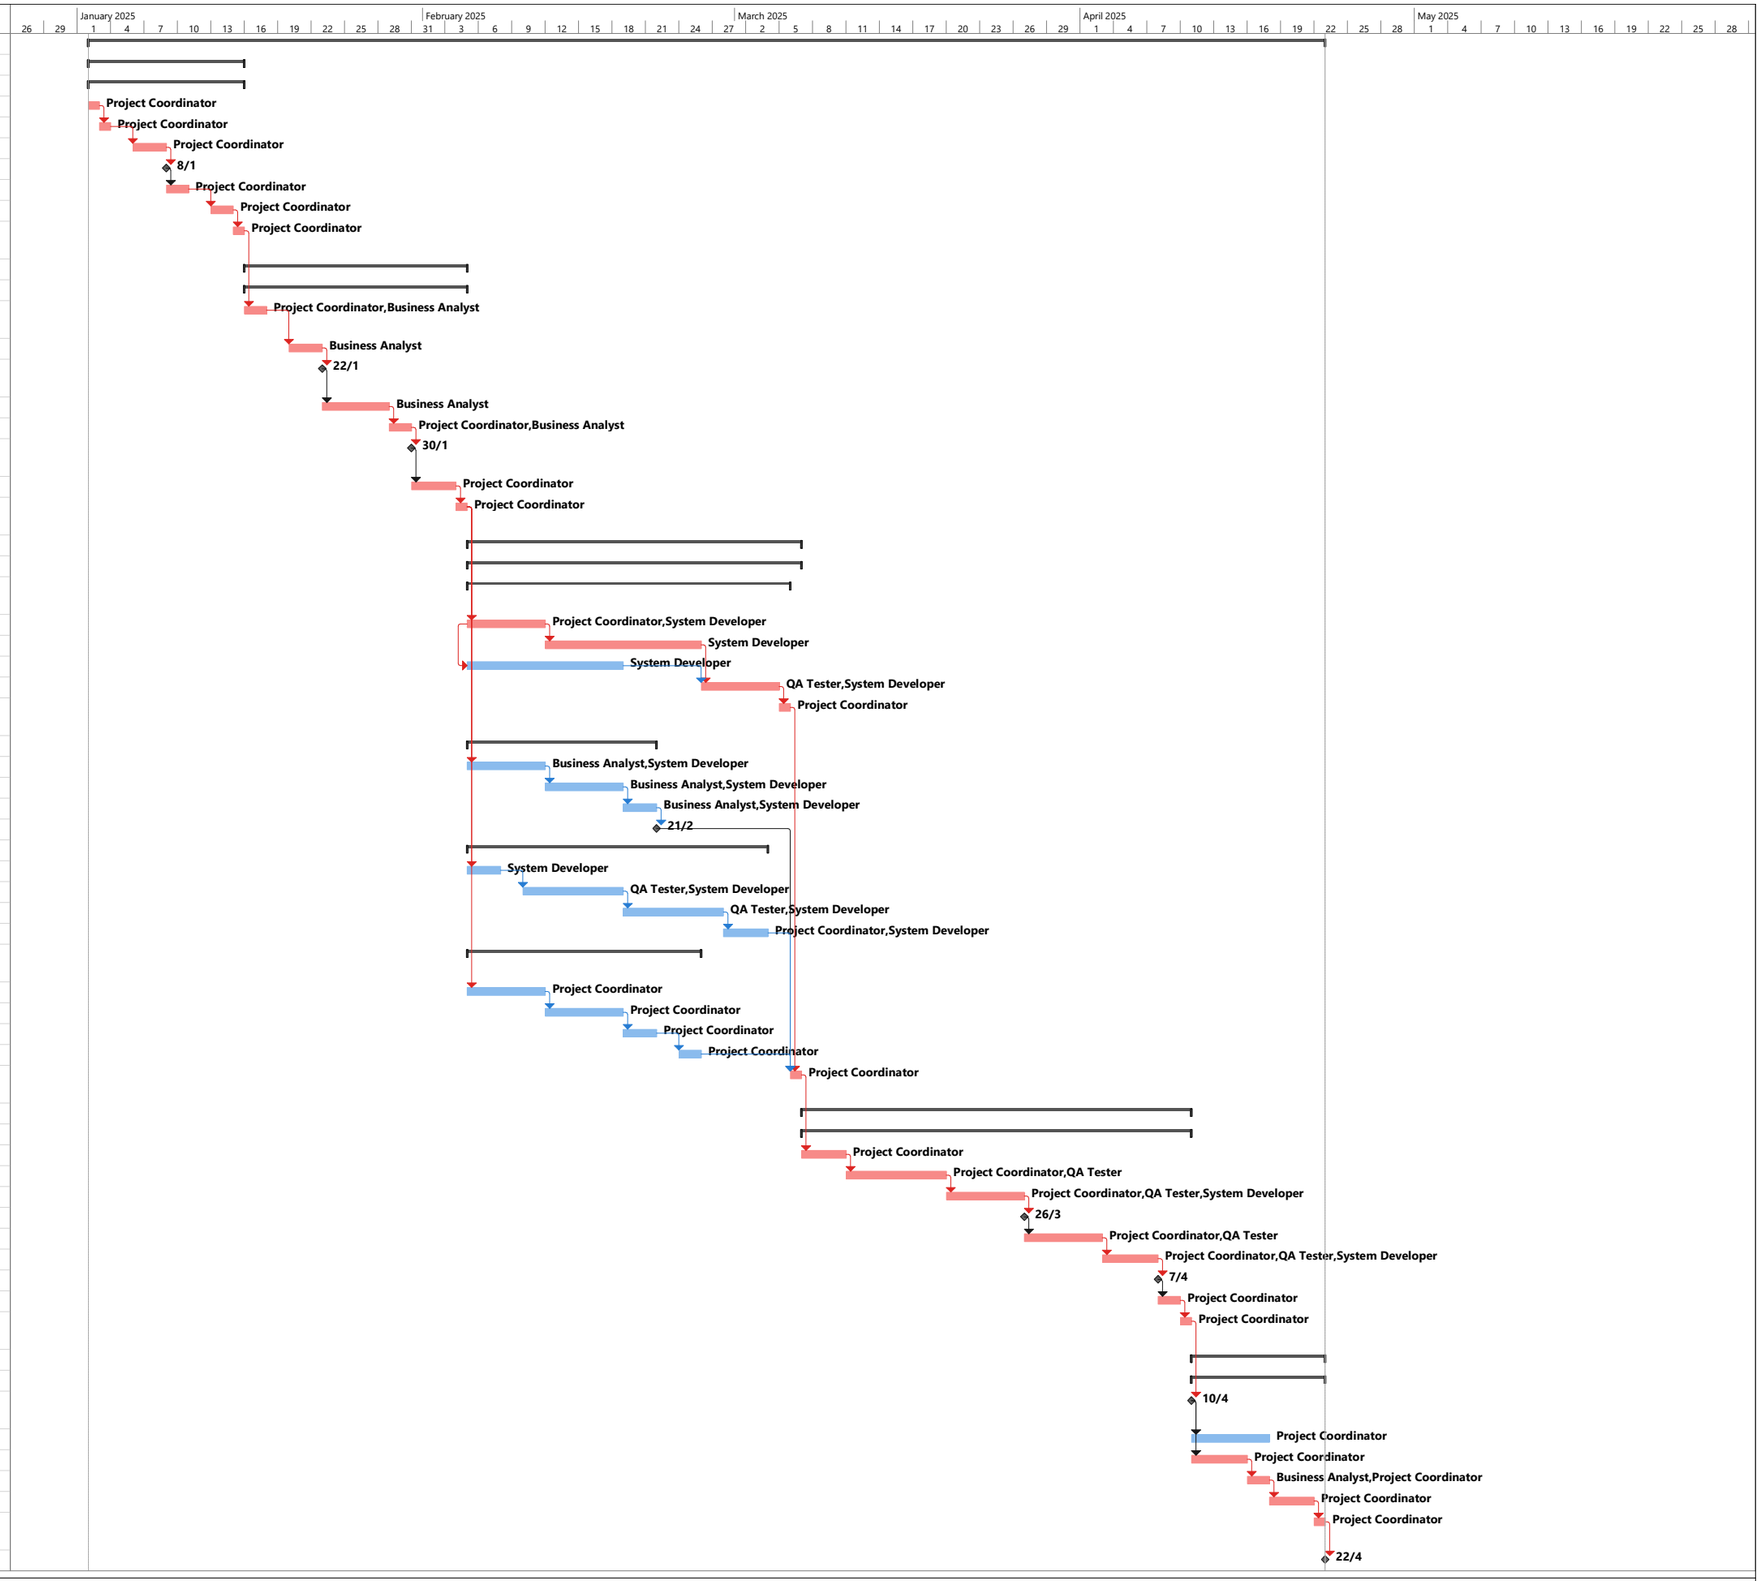

Project: Enterprise ICT System R
Date: Fri 13/3/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
